ID	Task Name	Duration	Start	Finish	Predecessors	Work
1	**Informe Preliminar**	**7.63 days?**	**Tue 3/23/10**	**Tue 3/30/10**		**0 hrs**
2	Elaboración Informe Prelimir	7.13 days?	Tue 3/23/10	Tue 3/30/10		0 hrs
3	Entrega informe preliminar	0 days	Tue 3/30/10	Tue 3/30/10	2	0 hrs
4	**Modelado del Negocio**	**13.25 days?**	**Wed 3/31/10**	**Tue 4/13/10**		**0 hrs**
5	Elaboración del modelo de n	12.25 days?	Wed 3/31/10	Mon 4/12/10		0 hrs
6	Presentación del modelo de	0 days	Tue 4/13/10	Tue 4/13/10	5	0 hrs
7	**Primera Iteración**	**58.63 days**	**Thu 4/15/10**	**Tue 6/15/10**		**261.2 hrs**
8	FT de requerimientos	175 hrs	Thu 4/15/10	Fri 5/7/10		31 hrs
9	FT de análisis	191.8 hrs	Mon 4/19/10	Fri 5/14/10	8SS+4 days	31 hrs
10	FT de diseño	221 hrs	Fri 4/23/10	Sat 5/22/10	9SS+4 days	75 hrs
11	FT de implementación	38 days	Tue 4/27/10	Sun 6/6/10	10SS+4 days	108 hrs
12	FT de prueba	40 days	Sat 5/1/10	Sat 6/12/10	11SS+4 days	16.2 hrs
13	Revisión preliminar	0 days	Tue 5/11/10	Tue 5/11/10		0 hrs
14	Presentación	1 day	Tue 6/15/10	Tue 6/15/10	8,9,10,11,12	0 hrs
15	**Segunda Iteración**	**76.38 days?**	**Wed 6/16/10**	**Sat 9/4/10**		**0 hrs**
16	FT de requerimientos	43.25 days?	Wed 6/16/10	Sat 7/31/10		0 hrs
17	FT de análisis	45.75 days?	Mon 6/28/10	Sat 8/14/10	16SS+4 days	0 hrs
18	FT de diseño	45.75 days?	Mon 7/5/10	Sat 8/21/10	17SS+4 days	0 hrs
19	FT de implementación	39.13 days?	Mon 7/19/10	Sun 8/29/10	18SS+4 days	0 hrs
20	FT de prueba	30 days?	Wed 8/4/10	Sat 9/4/10	19SS+4 days	0 hrs
21	Presentación	0 days	Sat 9/4/10	Sat 9/4/10	16,17,18,19,20	0 hrs
22	**Tercera Iteración**	**46.38 days?**	**Wed 9/1/10**	**Tue 10/19/10**		**0 hrs**
23	FT de requerimientos	23.88 days?	Wed 9/1/10	Sun 9/26/10		0 hrs
24	FT de análisis	25.88 days?	Mon 9/6/10	Sun 10/3/10	23SS+4 days	0 hrs
25	FT de diseño	25.88 days?	Mon 9/13/10	Sun 10/10/10	24SS+4 days	0 hrs
26	FT de implementación	23.88 days?	Wed 9/22/10	Sun 10/17/10	25SS+4 days	0 hrs
27	FT de prueba	6 days?	Mon 10/11/10	Sat 10/16/10	26SS+4 days	0 hrs
28	Presentación	0 days	Tue 10/19/10	Tue 10/19/10	23,24,25,26,27	0 hrs
29	Revisión General	13.25 days	Wed 10/20/10	Tue 11/2/10	28	0 hrs
30	Presentación Final	0 days	Tue 11/2/10	Tue 11/2/10	29	0 hrs
31	**Cuarta Iteración**	**265 days**	**Thu 3/3/11**	**Wed 12/7/11**		**0 hrs**
32	FT de requerimientos	195.75 days?	Thu 3/3/11	Sun 9/25/11		0 hrs
33	FT de análisis	163.63 days?	Wed 4/13/11	Mon 10/3/11	32SS+4 days	0 hrs
34	FT de diseño	159.63 days?	Sun 5/8/11	Mon 10/24/11	33SS+4 days	0 hrs
35	FT de implementación	121.88 days?	Fri 7/1/11	Mon 11/7/11	34SS+4 days	0 hrs
36	FT de prueba	78.5 days?	Sun 8/21/11	Fri 11/11/11	35SS+4 days	0 hrs
37	Presentación	0 days	Sat 11/12/11	Sat 11/12/11	32,33,34,35,36	0 hrs
38	Revisión General	22.88 days	Mon 11/14/11	Wed 12/7/11	37	0 hrs
39	Presentación Final	0 days	Wed 12/7/11	Wed 12/7/11	38	0 hrs

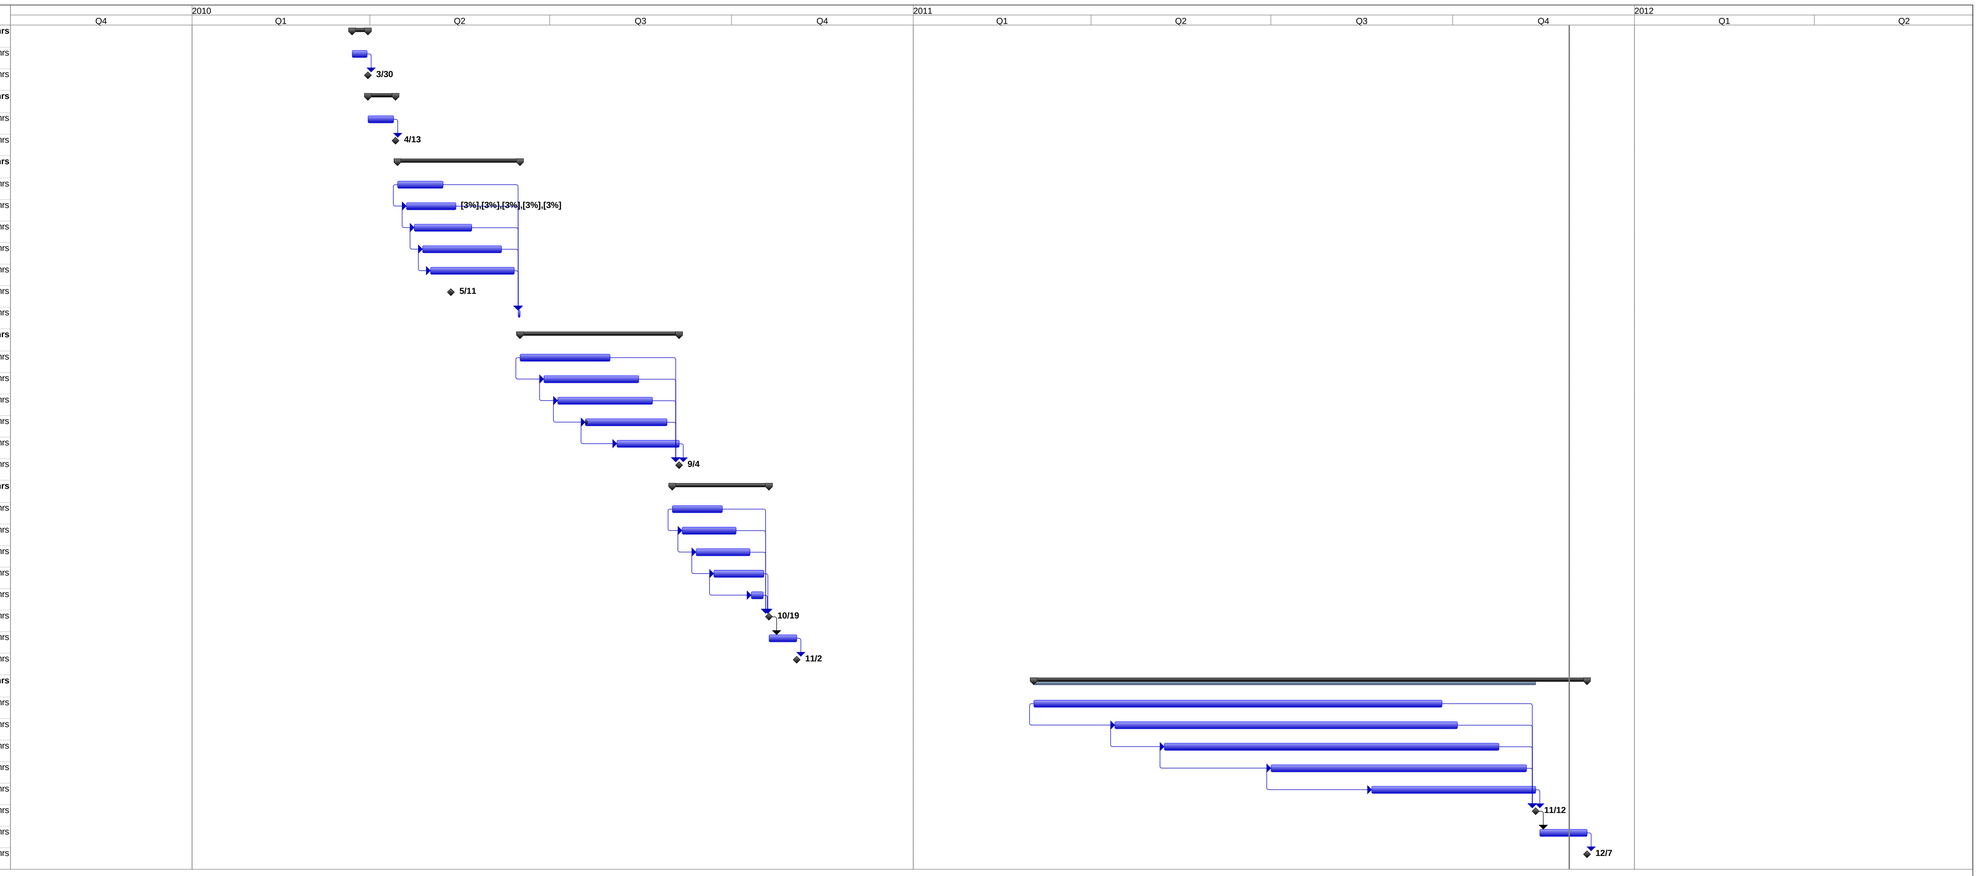

Project: Project1
Date: Tue 11/29/11

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Progress | Deadline
